


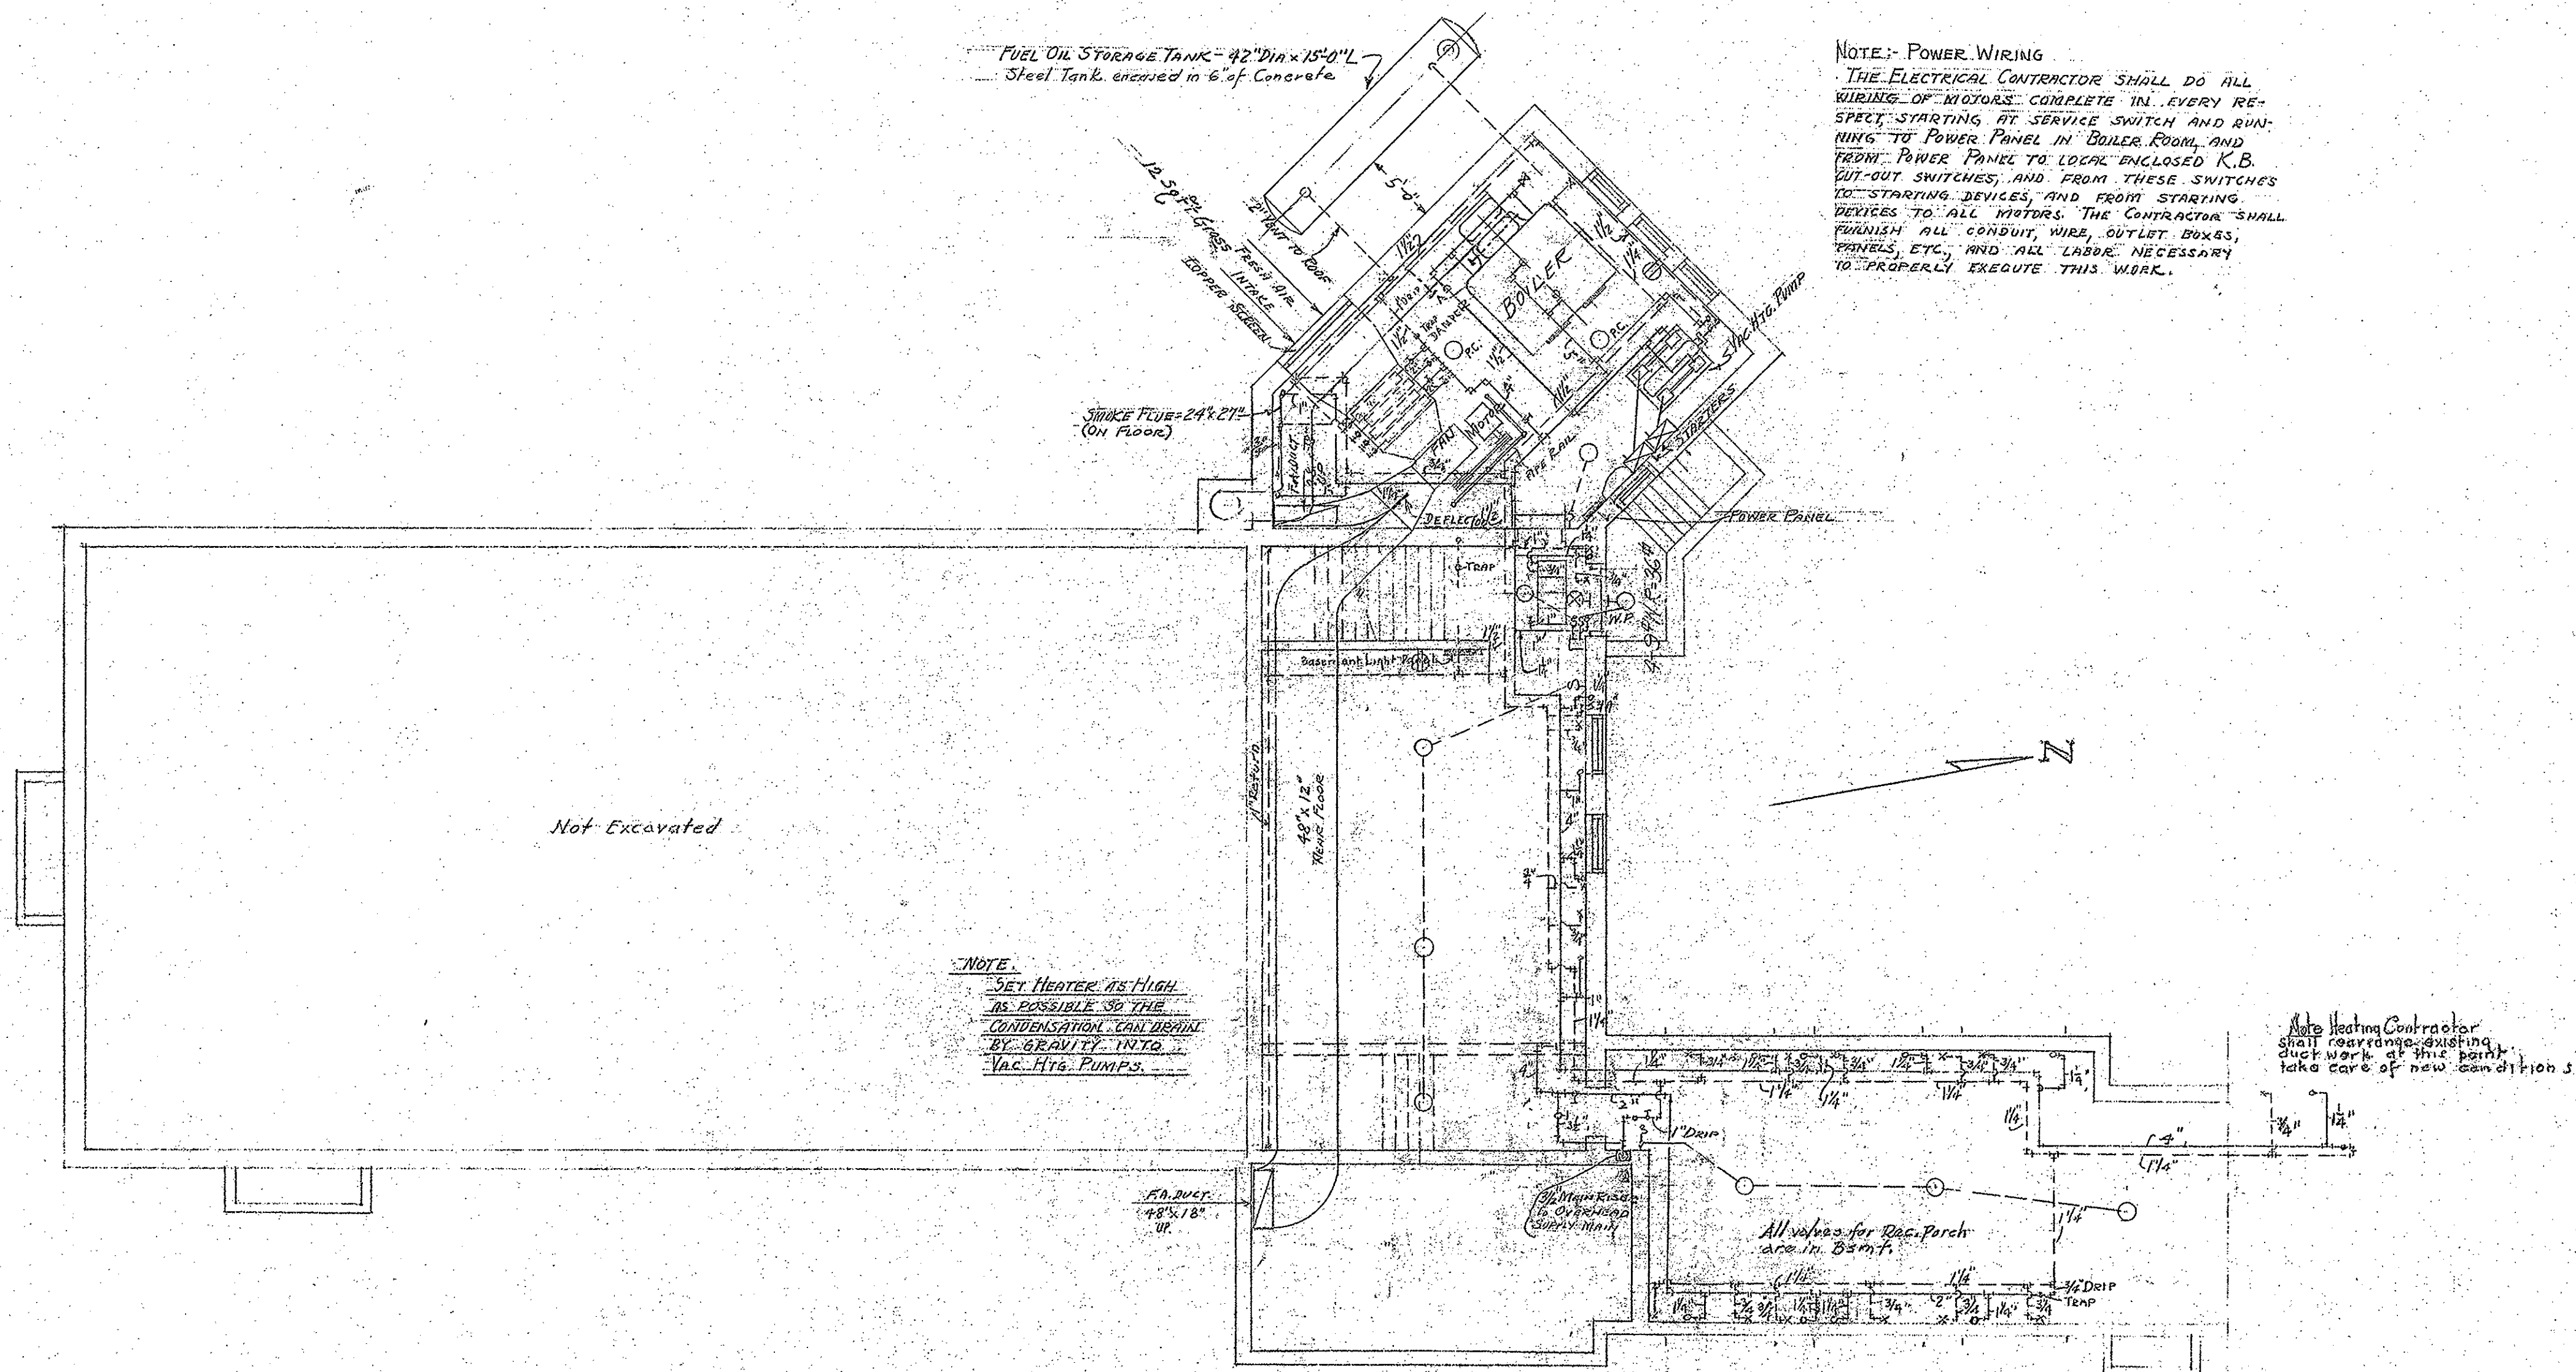

NOTE: POWER WIRING
THE ELECTRICAL CONTRACTOR SHALL DO ALL WIRING OF MOTORS COMPLETE IN EVERY RESPECT STARTING AT SERVICE SWITCH AND RUNNING TO POWER PANEL IN BOILER ROOM, AND FROM POWER PANEL TO LOCAL ENCLOSED K.B. OUT-OUT SWITCHES, AND FROM THESE SWITCHES TO STARTING DEVICES, AND FROM STARTING DEVICES TO ALL MOTORS. THE CONTRACTOR SHALL FURNISH ALL CONDUIT, WIRE, OUTLET BOXES, PANELS, ETC., AND ALL LABOR NECESSARY TO PROPERLY EXECUTE THIS WORK.

NOTE:
SET HEATER AS HIGH AS POSSIBLE SO THE CONDENSATION CAN DRAIN BY GRAVITY INTO VAC. HTS. PUMPS.

Note Heating Contractor shall rearrange existing duct work at this point, take care of new conditions.

1	10-4-28	Switch for stair light relocated. Set 3/4" Main Riser into wall below Recreation Porch. Added piping for heating of skylight in Recreation Porch above.
---	---------	---

NO	DATE	REVISIONS
----	------	-----------

YORK & SAWYER ARCHTS 100 E 42 ND ST NEW YORK	GYMNASIUM FOR MISS HALL'S SCHOOL PITTSFIELD MASS.	BASEMENT PLAN	H.E.01.
FRANK SUTTON CONS. ENGR 140 CEDAR ST NEW YORK		SCALE 1/8"=1'-0" DATE MAY 23, 1928	
